
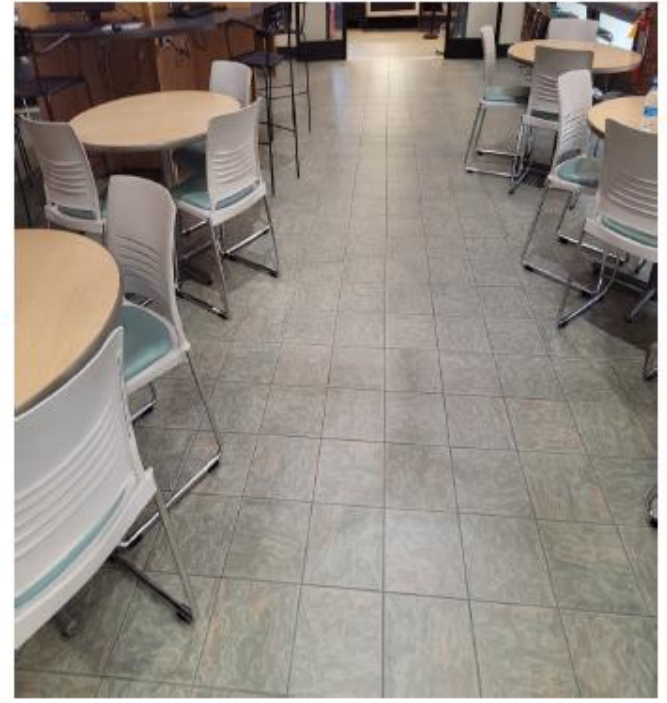


FACILITIES FY24 SUMMER MAJOR PROJECTS

- **JKB** - Main Theater renovation – involves new seating, lighting, paint, which will require the space to be offline for the Summer. Completion will be late Summer, depending on supply chain. done
- **Annex** – Campus Safety relocation – Requires renovations to the east side of the first floor. Work will be noisy at times and expected to be completed mid-August. done
- **Palamountain & North Hall** – lower lot paving – Paving to be completed the week of 5/20 with seal coating and restriping of lower Palamountain lot to occur during the Summer. done
- **Wilmarth Hall** – shower overhaul- Work beginning 5/20 and expected to be completed early August. Some supplies will be stored between Ladd and Wilmarth. done
- **Wilmarth Hall** – new air handler and hot water system- Work to commence 5/15 which be on the exterior to dig and create an opening to allow for the new equipment to be installed. Interior replacement of the HVAC systems to begin on 5/20 and be completed early August. Fencing will be installed around the McClellan, Starbuck and Wilmarth area. done
- **Weicking Hall** – new hot water system- Work to occur in the lower mechanical room with some welding outside. We anticipate completion by early August. The new hot water system will be tied to the geothermal well system.
- **Case & Dining Hall** – sidewalk and post replacement – Work is scheduled to begin immediately after Reunion weekend and extend to late August. The work will be noisy and have the area between Case and the Dining hall fenced off for the Summer. Additionally, we will fence off the area between Ladd and Wilmarth and some parking spaces in Case to allow for truck traffic on a daily basis. The CDTA bus stop will have to be temporarily relocated.
- **McCaffery-Wagman Tennis and Wellness Center** – Work will be on going and will include closing of the main entrance sidewalk for the Summer. We will redirect people to the side entrance similar to last Summer.
- **Baseball field** – relocation – Working on final approvals from the Town and anticipate this work to begin in mid-June. Started in June
- **CIS** – final move ins- Movers will be completing their work the week of 5/20 with Faculty working on final set ups over the Summer. Facilities is working with Faculty to complete minor work over the Summer including the construction of two future rooms.
- **Sussman & Northwoods** – ADA apartment renovations – In an effort to improve accessibility in the apartments Facilities will be performing renovations to one Sussman Hillside apartment and one Northwoods apartment. Work is scheduled to start in early June and expected to be completed before students return. done

- **Campus-wide** – concrete repairs - During the Summer Facilities will have sidewalks repaired/patched to address trip hazards. This work could occur on daily basis but we will have proper safety cones around the affected areas. done
- **Case Center** – major electrical switch gear upgrade- Currently waiting on equipment but anticipate installing in June or July on a weekend. We will notify the staff in Case and the Library prior to commencing since the power will be shut down for approximately hours to safely complete this work. The location of the gear is near the ramp leading to Case walkway. done
- **Academic Classroom** – renovation upgrades – The rooms have been taking out of service for the Summer and will be completed prior to the Fall. Work may include carpet refresh, painting, white boards and or furniture.
- **Residential Halls** – interior painting – The buildings are being identified next week and with the work being scheduled around occupancy.
- **Palamountain** – Auditorium lighting replacement - The material is being sourced but anticipate completing in July/August. Facilities will coordinate with EMS when this work can be completed. If there are too many conflicts we may schedule for winter break.
- **North Woods** – replacement of 22 heat pumps (buildings 1 &2) and all new appliances- The buildings have been identified and taking out of service for the Summer. We have the work starting at the end of May with completing occurring around the 2nd week of August.
- **Weickling Hall** – LVP/LVT flooring upgrades - The building has been scheduled to be vacant to allow this work. We anticipate completing by early August.
- **Tang** – fire alarm replacement- Equipment has been ordered. Installations is being coordinated with the Tang staff and expected to occur in June/July.
- **Dining Hall** – heat pump replacement – Scheduled for 7/10-7/16 -Ladies room (to allow access to equipment) will be closed and a crane will be located in the parking lot)- This is being coordinated with the Dining hall staff.
- **Zankel** – glass replacement – (coat room to office renovation) – Waiting on availability from glass vendor. Once known facilities will work with the Zankel staff to schedule install. Install may require a lift that may affect pedestrian pathways but safety cones will be provided.
- **Howe/Rounds** – dumbwaiter replacement – Equipment has arrived and now anticipate the work being completed in June/July. We will work with Summer housing to schedule and notify occupants if needed.
- **CIS North Observation Deck**- Installing an donor funded observation deck that will be utilized for classes/astronomy.

** Listed above are some of the major projects Facilities will be undertaking this FY24 summer, please note, this list is not all inclusive, and there are many minor projects also in progress.

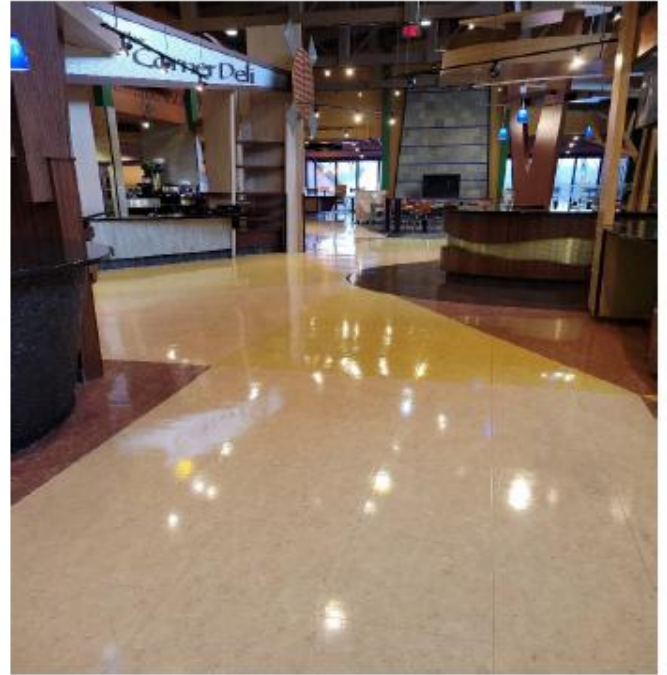

Cleaning, polishing and shampooing of carpets







Painting of the Wycoff Center





New AC unit installed




New Domestic hot water boiler installed

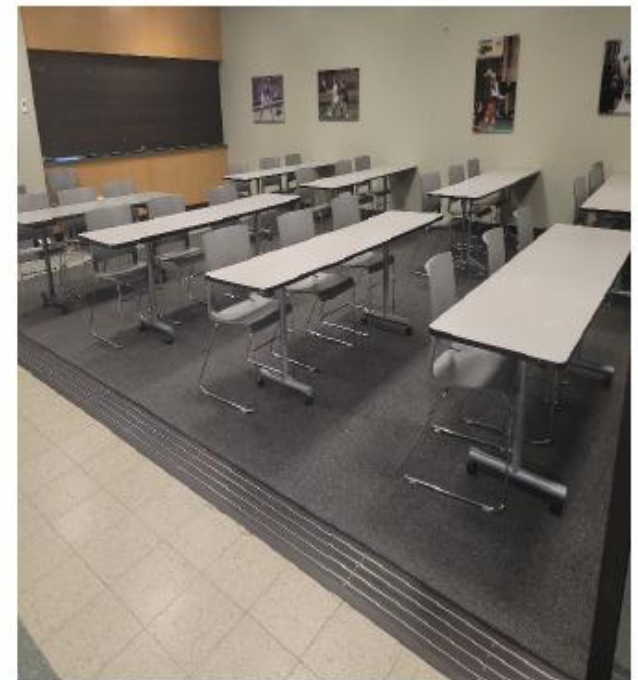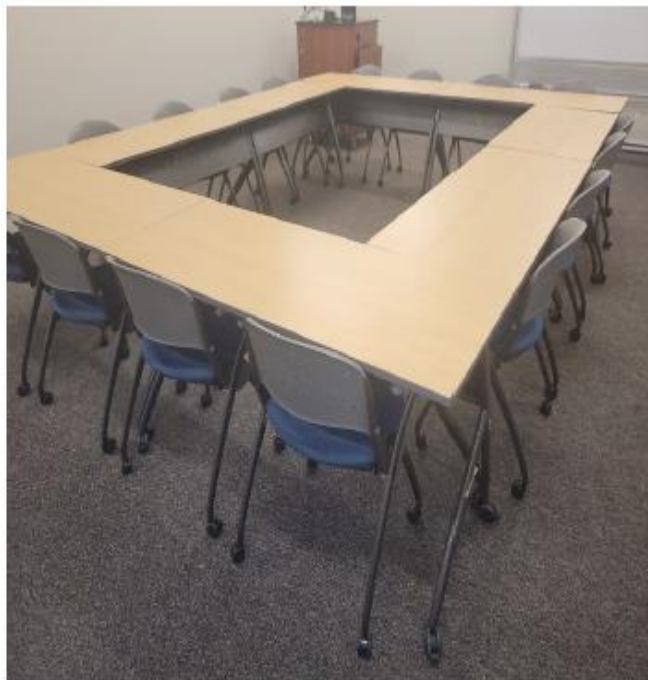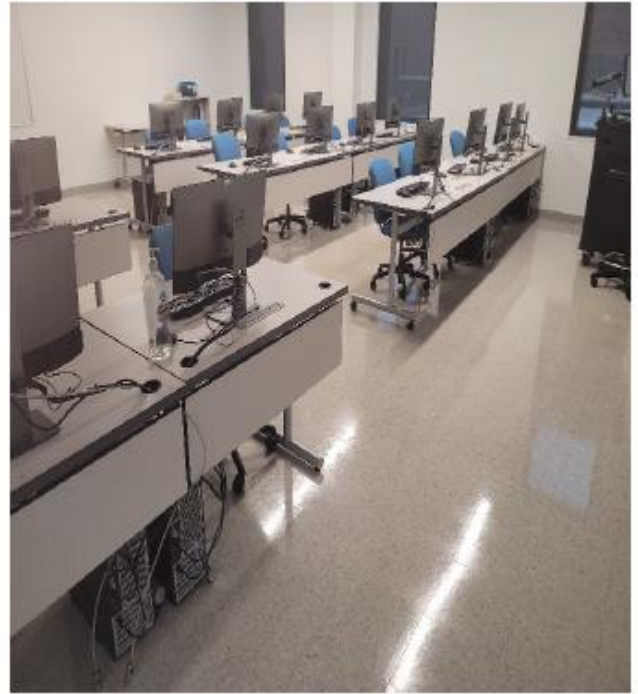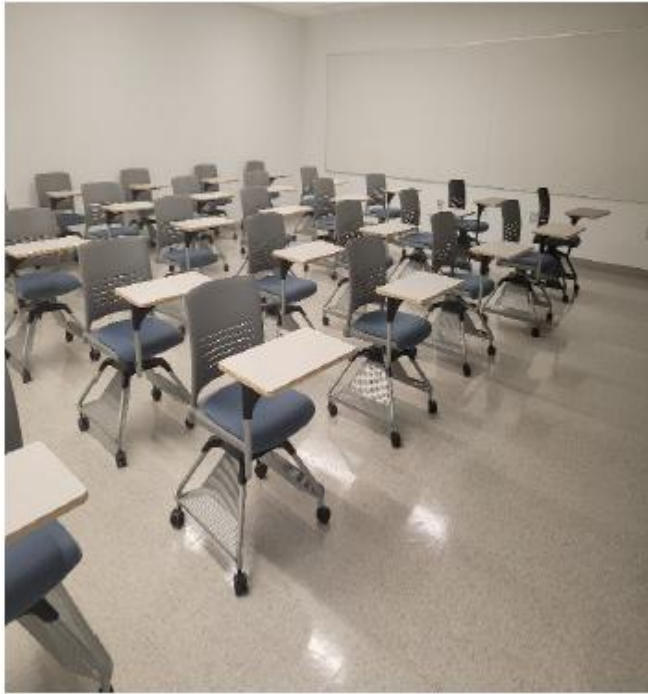


Classroom renovations

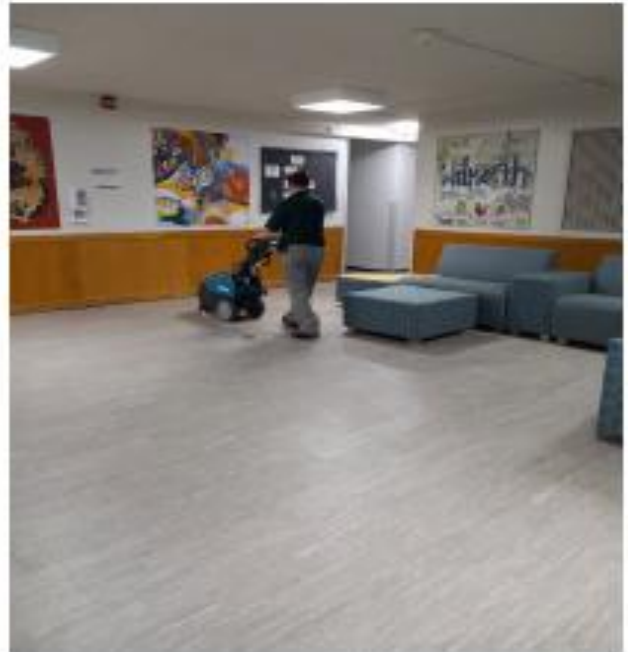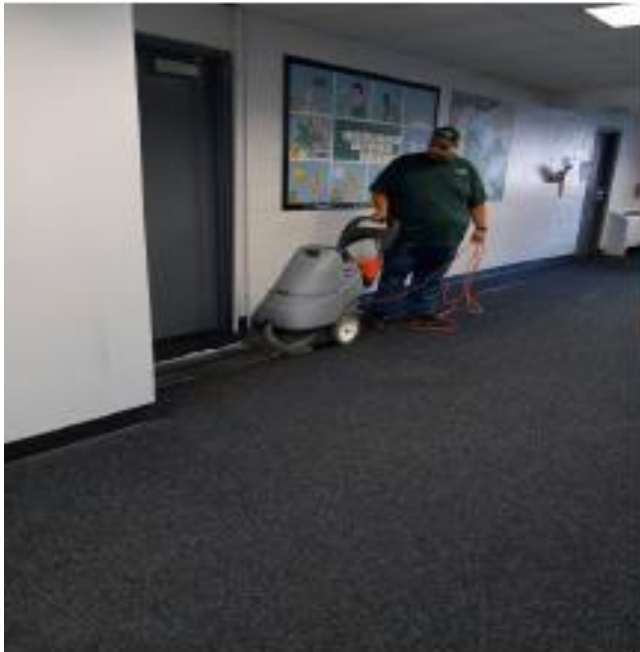

Residential Hall refresh – painting and new floors

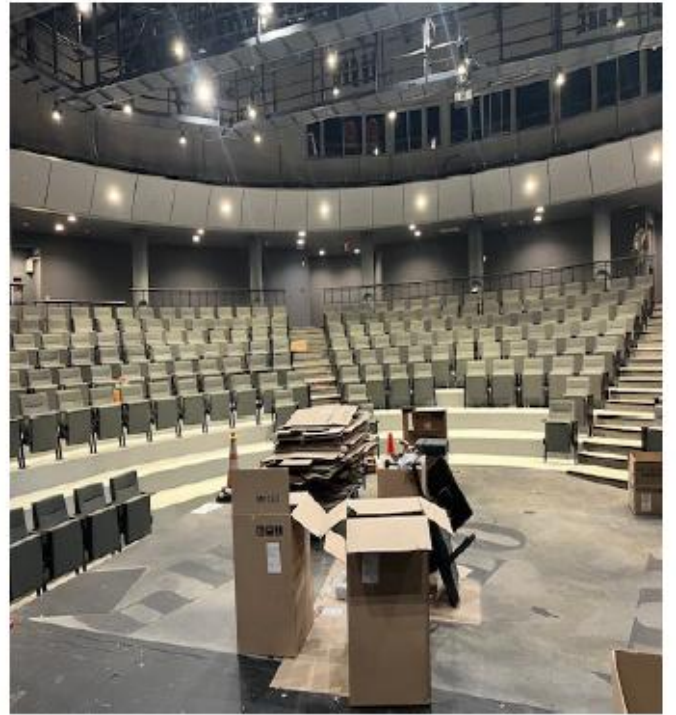

JKB Theater renovations

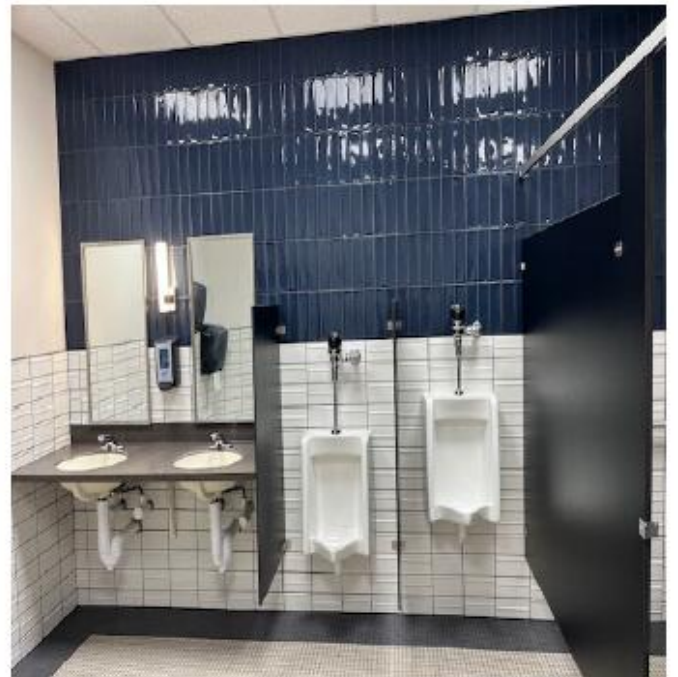

Bathroom renovations



Case Center walkway renovations



Horse washing station



Working on new baseball field site
